


Upper Lawrenceville Waterline Replacement Project – Phase 2

PROGRESS AND LOOK-AHEAD:

- To date, 8-inch water main has been installed on Holmes Street from Stanton Avenue to 54th Street, Carnegie Street from Stanton Avenue to 52nd Street, Keystone Street from 54th Street to 55th Street, and 55th Street from Keystone Street to Carnegie Street.
- To date, service lines have been connected to the new water main on Holmes Street from Stanton Avenue to 54th Street and Carnegie Street from Stanton Avenue to half way to 52nd Street.
- During the week of August 1st, 2016, the new water main on Keystone Street from 54th Street to 55th Street and 55th Street from Keystone Street to Carnegie Street will be pressure tested and disinfected.
- Recently, installation of 8-inch water main has commenced on Duncan Street.
- Questions? Please contact:
Tunde Ibrahim
PWSA Construction Project Manager
(412) 255-2545 or
rtunde@pgh2o.com

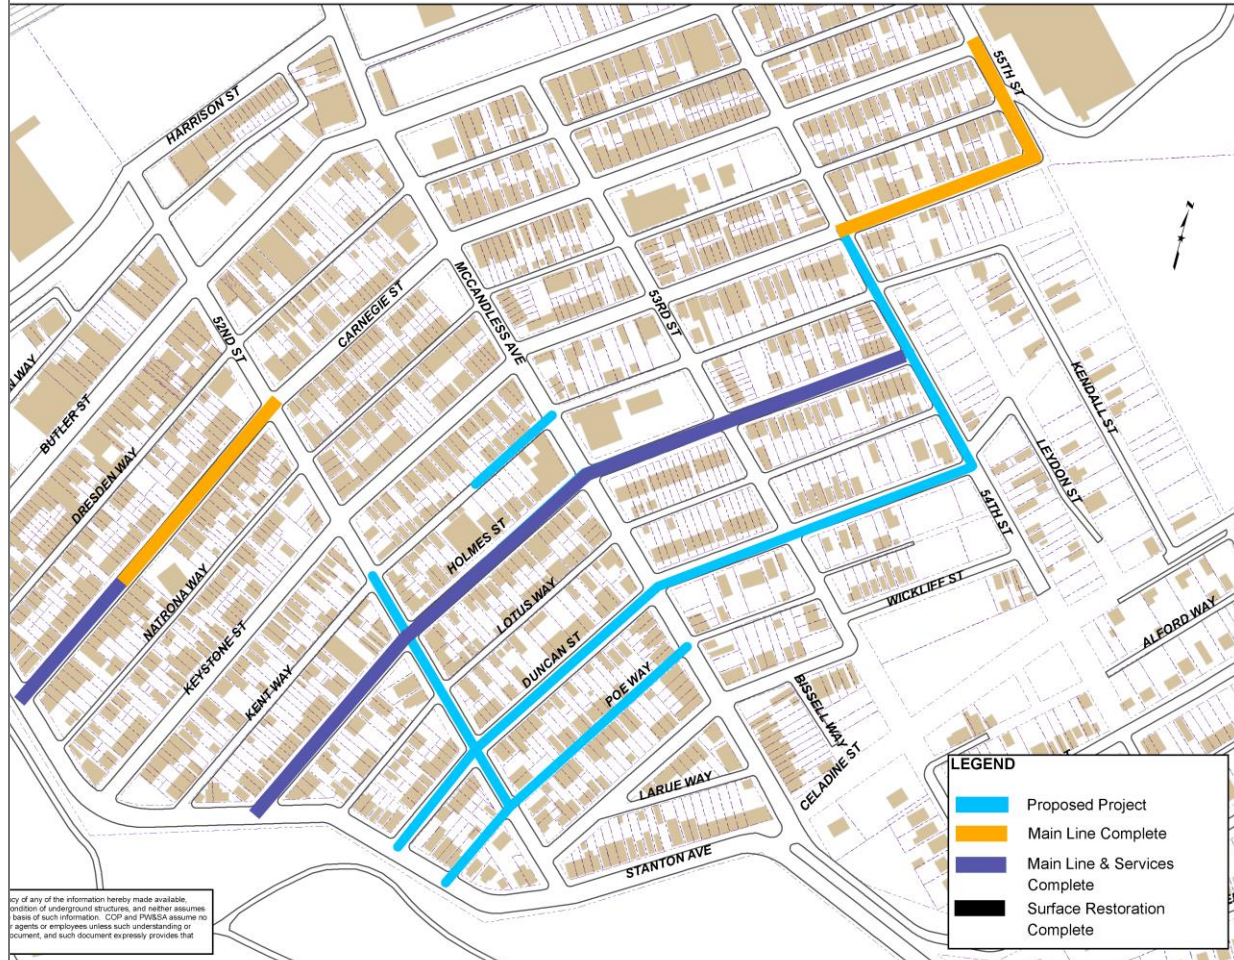

Accuracy of any of the information hereby made available, position of underground structures, and neither assumes basis of such information. CDP and PWSA assumes no agents or employees unless such understanding or agreement, and such document expressly provides that
